STATEMENT OF WORK

Construction 101 Introduction to Construction Site Visits and Processes

EME 6631 Managing Instructional Development

Kim Gabbard, Rebecca Yost, and Jordan Gonzalez

October 26, 2025

Table of Contents

Introduction *2*

Project Schedule and Scope *2*

Scope of Work 2

Scope Control and Validation 3

Deliverables 3

Work Breakdown Structure (WBS) 4

Task Schedule, Dates, and Task Owners 4

Project Team *6*

Team Structure 6

Roles and Responsibilities 7

Resource and Cost Requirements *8*

Risk Management Plan *9*

Defining Risk 9

Risk Management Approach 9

Identifying Risks 9

Risk Matrix 10

Risk Mitigation Strategies 10

Ongoing Monitoring 11

Summary of Risk Management Plan 11

Sponsor Acceptance *11*

Appendices *12*

Introduction

This project will introduce FSU students to construction site visits, processes, and safety expectations through a proposed 8-week, self-paced, asynchronous course to be built and housed within the Canvas platform for the FSU Real Estate Center. The goals of the project are to:

- Improve awareness of construction culture and etiquette.
- Emphasize the importance of safety when visiting or working near construction sites.
- Provide a foundational understanding of project estimates, permitting, construction processes, and inspections.
- Equip learners with practical knowledge of construction terminology, documents, and expectations.

This document will describe the scope of work, project team structure and decision-making processes, detailed schedule, resource and cost requirements, and will outline key risks to the progress success as well as mitigating actions.

Project Schedule and Scope

This section describes the project scope, purpose, goals, and objectives. It also presents a high-level list of project deliverables, a work breakdown structure and detailed schedule, and describes a process for how scope change requests will be addressed.

Scope of Work

The vision for the course is to provide FSU Real Estate and Urban Planning students with a unique and easily accessible opportunity to gain foundational knowledge and practical skills to navigate construction sites safely, understand processes, and engage confidently with stakeholders.

The course will contain interviews with professionals in the field, site walkthroughs, interactive content, assessments, and reflective exercises. The project will be expected to launch for students in August 2026, with key interim milestones in May 2026 and January 2026.

The project team will create the course in Canvas with a home page, eight modules including instructional contents, videos, interactive activities and assessments. A full outline of the course content can be found in Appendix A.

Additionally, contracted services will be utilized for two deliverables that cannot be created with existing resources. A Bluebeam technician will be contracted to create interactive blueprints that can be embedded into the course, and a videographer will shoot interviews and site visits on location for video instruction. A sample Scope of Work document for videography services is provided in Appendix B.

Scope Control and Validation

To manage project scope and create clear pathways to approve changes to the project plan, a control process will be initiated using a Scope Change Request Form (see Appendix C). Approvals will be required from the Project Manager and Sponsor to make changes to the identified scope of work.

Deliverables

The deliverables for the project are outlined below.


Table 1. Project Deliverables

Item	Components	Description
Instructional Content	• Instructional text • Instructional resources • Instructional activity prompts	• Written instructional content for 8 weekly modules • Locate or provide instructional resources (videos, blueprints, safety guides, org charts) • Discussion prompts, reflection prompts, simulation goals, terminology
Videos	• Scripts and/or storyboards • Time on location • Images and slide deck • Bumpers and/or lower-thirds • Video recording, editing and captioning	• Scripts for lecture content or storyboards for site visits or walkthroughs that will be recorded/edited • Site visits for recording • Supplementary video resources that should be shown on-screen • Intro and closing bumpers for branded content and branded introductions for interviews • Videographer to edit content recorded on-site or video tools used by ID team to produce video content
Interactives	• Interactive blueprints (Bluebeam) • Interactive learning materials (H5P, Canva, PPT) • Simulations	• Demolition plans and floor plans, identifying types of marks • Identifying safety violations, appropriate attire, matching terminology and roles, cost charts, timelines, flashcards • Inspection checkpoints, safety violations
Course build	• Canvas course build • Interactives build • Dashboard build	• Full 8-module course build in Canvas with styling • Content build for interactive learning materials • Create dashboard to monitor enrolments and learner progress
Implementation	• Quality assurance and evaluation • Grading & feedback	• Review course build for technical errors, content errors, accessibility, stakeholder approvals • Create facilitator training for review of DBLA replies, reflections, and assessments

Work Breakdown Structure (WBS)

The work breakdown structure below describes the major high-level tasks to accomplish the Construction 101 project, but some high-level tasks also have sub-tasks. For example, 3.1 - Gather instructional content also includes a subtask for the Instructional Designer (ID) to provide a template to the SME to provide the content, and a subtask for the Instructional Content Developer (ICD) to source existing instructional resources, and a separate subtask for review and verification period to ensure quality and accuracy.

Figure 1. Construction 101 Work Breakdown Structure

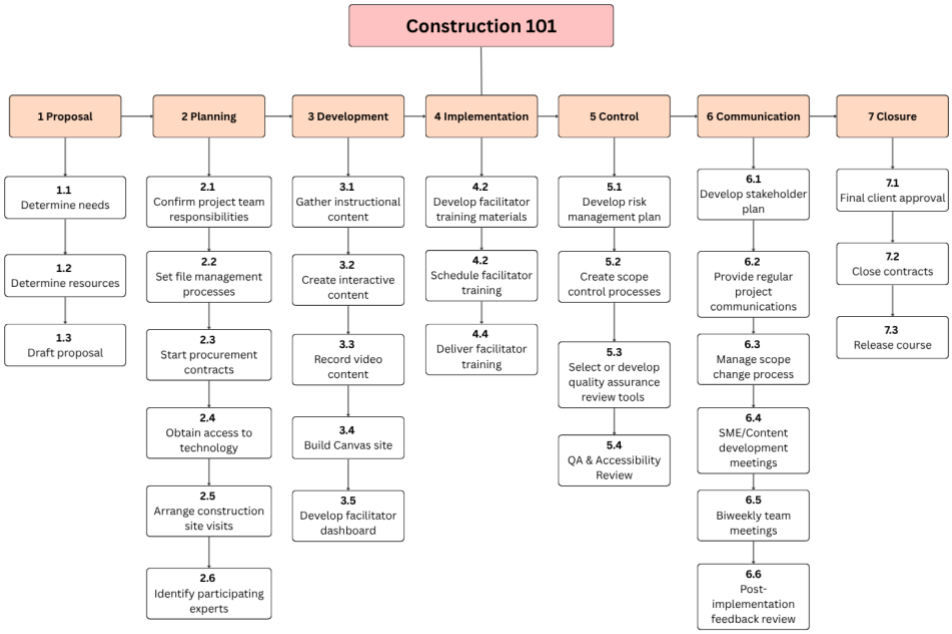

Additional sub-tasks within the Development section are further broken out in the Construction 101 Monday board and Gantt chart (see Appendix D).

Task Schedule, Dates, and Task Owners

To facilitate timely completion and efficiently manage the work established in the work breakdown structure, a list of major project milestones has been compiled below.

Table 2. Project Milestones and Responsibility

Milestone	Date	Description	Owner
Initial approval	Sept 28, 2025	Approval required to move ahead with video contracting and other vendors.	Project Manager
Content delivery	Nov 26, 2025	All instructional content provided by SME, including lecture scripts.	Subject Matter Expert (SME)

Off-site visits	Dec 2, 2025	Construction site visits scheduled. These visits should take place while the weather is still good in Dec-Feb.	Project Manager
Video contract	Dec 2, 2025	Videographer contract signed. Interview-style videos recorded as location and interviewer availability permits between Dec-Feb and allows time for post-processing.	Project Manager
Interactive content storyboard	Jan 5, 2026	Storyboards for interactive content developed for approval.	Instructional Content Developer (ICD)
Course prototype	Jan 19, 2026	One completed module created for client initial review and feedback.	Instructional Designer (ID)
Video content	March 2, 2026	All video content received. Videos will need to be delivered to complete the course build with adequate time for captioning.	Videographer
Interactive content	April 4, 2026	All interactive content developed and available for inclusion in the course.	ICD
Course build	April 20, 2026	Complete course build and data analytics dashboard complete. Will need time for testing.	ID
Course content evaluation	May 4, 2026	Final review period begins for faculty reviewers, approvals and edits. Reviewers will need summer months to review content and provide feedback between regular semesters.	Review Group
Accessibility review	June 1, 2026	Final accessibility and quality assurance check begins. Extra time is needed to identify and rectify accessibility issues.	Accessibility Reviewer
Final revisions	Aug 1, 2026	All final content and accessibility updates must be completed to allow revision and updates to course materials.	ID/ICD
Course handoff and training	Aug 14, 2026	The course should be handed over to clients and available for students by the beginning of the Fall 2026 semester.	Project Manager
Contract closure	August 31, 2026	All external vendors contract closure and payment.	Project Manager
Feedback review	Dec 1, 2026	Monthly reports generated and distributed to stakeholders for ongoing review.	Project Manager

Detailed sub-tasks, owners, and due dates based on the work breakdown structure are outlined in a Monday board. A concise visualization of major tasks, owners, and project progress can be found in Appendix E, The One-Page Project Manager (OPPM). An updated copy of the OPPM will be distributed in regular stakeholder communications and project updates.


Project Team

The project's team structure, roles, and responsibilities are described in the next section, including a framework for operational decision-making.

Team Structure

The reporting lines between the key roles are outlined in Figure 1. In addition to the key roles, the figure also includes the videographer who will be working under the Instructional Content Developer.

Figure 2. Project Organization Structure

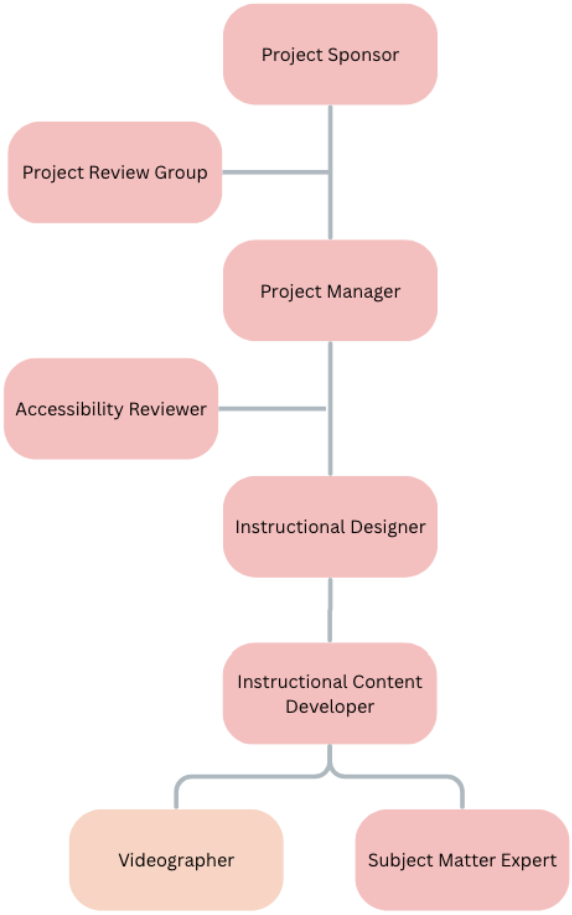

This project operates under a three-part decision authority structure: Operational, Content and Instructional, and Strategic and Institutional. This structure is outlined in Table 3.

Table 3. Decision Authority Structure

Decision Type	Roles Involved	Focus
Operational	PM, ID, Instructional Content Developer	Day-to-day coordination, logistics, and progress tracking
Content and Instructional	PM, SME, ID, Instructional Content Developer, Review Group, Accessibility Reviewer	Academic integrity, Instructional Design, and learner experience
Strategic and Institutional	Review Group, Project Sponsor	Vision, alignment, and resource approval

Operational decisions, such as assigning tasks and coordinating communication, are made collaboratively within the ID Team and are approved by the Project Manager. Decisions will be escalated to the Project Sponsor if the issue affects the project's scope, cost, or timeline.

Content and Instructional decisions will include decisions about learning design, accuracy, and quality. SMEs will review and validate content accuracy, and the Accessibility Reviewer will review the product for compliance before the product is sent to the Review Group for institutional review.

Strategic and Institutional decisions are ultimately made by the Project Sponsor. They are the approval authority of all decisions that affect scope, budget, timelines, and final deliverables. The Review Group will advise the Project Sponsor on the product's alignment with institutional goals.

The success of the project relies on the coordination of roles and sharing responsibilities. For example, the ID, Content Developer, and SME must collaborate closely on script development, activity design, and multimedia planning. The Project Manager, Content Developer, and Videographer must coordinate production schedules, deliverables, and post-production editing. The Accessibility Reviewer will need to support the ID team during testing and quality assurance to ensure all materials are compliant before the Review Group assesses the final product.

Roles and Responsibilities

An outline of the key roles required for this project is provided in Table 4 below.

Table 4. Project Roles and Responsibilities

Organization	Role	Responsibilities
FSU Real Estate Center	Project Sponsor	• Providing overall vision and strategic direction of the project. • Approving scope, timeline, and major deliverables of the project. • Securing support from FSU and connect ID team with SMEs. • Resolving high-level issues.

		• Providing final approval of the project.
	SME	• Ensuring content reflects accurate construction practices. • Advises on module topics, terminology, and case studies. • Reviews and approves instructional materials and assessments. • Provides examples and connections to industry professionals
ID Team	Project Manager	• Managing daily project activities, schedules, and communication between teams. • Managing project interdependencies. • Tracking and reporting risk, issues, and scope changes. • Facilitating stakeholder meetings.
	Instructional Designer	• Designing learning experiences for the course that align with course objectives. • Aligning activities and assessments to learning objectives. • Developing discussion and reflection prompts. • Ensuring course layouts and navigation support learning.
	Instructional Content Developer/ SME Coordinator	• Curating and adapting instructional resources. • Coordinating with videographer to develop multimedia content that supports learning objectives. • Collaborating with SMEs and ID to ensure accuracy and alignment with learning objectives and course goals
	Accessibility Reviewer	• Reviewing all content for WCAG 2.1 AA compliance. • Testing course navigation, visuals, and captions within Canvas. • Identifying and documenting technical and content errors for correction.
FSU Facilities	Review Group	• Providing feedback on instructional content, videos, and interactives. • Ensuring materials meet program and instructional requirements. • Verifying that all necessary client and vendor documentation is completed and approved before the project begins.

Resource and Cost Requirements

The project budget can be viewed in Appendix F. The instructional design and development work for this project will be completed in-house by the FSU ID team, which includes the PM, ID, Instructional Content Developer/SME Coordinator, and Accessibility Reviewer. As these roles are part of the internal FSU ID unit and are supported through existing institutional resources,

their work is not billed as an external cost and therefore does not include a monetary value in the project budget.

Risk Management Plan

Defining Risk

Project risks are potential events or conditions that may negatively impact scope, schedule, budget, quality, or project success. For the Construction 101 course, risks are driven by project dependencies such as multimedia production, subject-matter availability, construction site scheduling, vendor coordination, and LMS technology. When risks are identified early and continuously monitored, their impact on the timeline, cost, and quality can be minimized.

Each risk is evaluated based on (1) probability of occurrence and (2) impact severity. Mitigation strategies are implemented for risks rated Medium or High.

Risk Management Approach

To manage risks effectively throughout the project lifecycle, the Project Manager will:

- Monitor risks weekly during planning and execution phases
- Escalate High-impact risks to the Sponsor and Review Group for rapid resolution
- Maintain open communication with SMEs, videographers, site contacts, and stakeholders
- Track risks in the project log and update status through milestone reviews
- Encourage proactive reporting of risks by all team members and vendors

As previously outlined in the charter, the project has fixed milestones, a defined launch deadline, vendor dependencies, and technology requirements.

Identifying Risks

Risks for this project fall into six primary categories. Table 5 identifies and describes each of these categories.

Table 5. Types of Risks

Category	Description
Schedule/Time Risks	Delays in video production, site access, SME reviews, or content development
Quality Risks	Content accuracy, ADA compliance, and professional production standards
Technology Risks	LMS limitations, interactive tool failures, or media compatibility issues
Budgetary Risks	Vendor overtime, unexpected software or production costs
Resource/Personnel Risks	SME availability, stakeholder responsiveness, or turnover

Site/Operational Risks	Inability to secure or film at construction sites, weather delays, or safety restrictions

Risk Matrix

Table 6. Risk Matrix

	Impact		
Probability	**Low**	**Medium**	**High**
High	-	Timeline Delays	Technology Failure
Medium	Budget Overages	SME Availability	Site Access Failure
Low	Minor Edits	-	Safety or Compliance Issue

Risk Mitigation Strategies

In addition to the risk's impact and probability, Table X also describes the source of the risk and planned mitigation strategies.

Table 7. Risk Mitigation Strategies

Risk	Impact	Probability	Source	Mitigation Strategy
Timeline Delays	Medium	25%	Dependencies on video, SMEs, site scheduling	Weekly progress checks; lock milestone dates; initiate early filming windows
Quality/Accuracy Risks	High	30%	SME availability; construction complexity	Use multi-step reviews; require SME sign-off for all technical content
Technology/LMS Failure	High	15%	Canvas or interactive tool limits	Build and test prototype early; maintain fallback formats
Budget Overruns	Medium	20%	Vendor hours or equipment needs	Hold 10–15% contingency; pre-approve vendor scopes
SME or Stakeholder Availability	Medium	30%	Scheduling conflicts	Schedule reviews 2–3 weeks in advance; identify backup SMEs

Site Access or Weather Delays	High	10%	Campus access and weather conditions	Secure backup filming locations; record b-roll early

Ongoing Monitoring

The Project Manager will evaluate risks at each milestone and report changes in project status meetings. If a risk becomes an issue, a corrective action plan will be initiated immediately and documented.

Summary of Risk Management Plan

This proactive approach to risk identification and mitigation ensures that the Construction 101 course can be delivered on time, on budget and within Scope. By enforcing communication protocols, milestone discipline, and early technology validation, the project team reduces the likelihood that schedule, site logistics, or production challenges will impact the August 2026 launch.

Sponsor Acceptance

Approved by Project Sponsor:

_____ _____

FSU Real Estate Center Executive Director *Date*

Appendices

A. Project Content Outline
B. Scope of Work: Videographer
C. Scope Change Request Form
D. Construction 101 Gantt chart
E. One-Page Project Manager (OPPM)
F. Project Budget

Appendix A-Project Content Outline

Course Title: Introduction to Construction Site Visits and Processes

Week 1 – Orientation & Safety Culture

Topics

Course overview & expectations

Construction site etiquette: Be on time, wear identifying items

Importance of safety rules and boundaries: What to wear on site, don't touch anything

Media/Content

Welcome video

Reading: Safety culture guide (PDF handout)

Interactive scenario: "Spot the safety violation" (images or short clips)

Assessments

Safety quiz (multiple choice, true/false)

Introductions forum: learners share prior experiences or concerns about site visits

Week 2 – Roles in Construction Teams

Topics

General contractor, superintendent, subcontractors, project manager

Team dynamics on site

Media/Content

Short video interviews with professionals in each role

Reading: Organizational chart & responsibilities document

Case study: "A day in the life of a project manager"

Assessments

Matching exercise (roles vs. responsibilities)

Discussion board: Why are clear roles critical for safety & efficiency?

Week 3 – Construction Estimates & Value Engineering

Topics

Components of an estimate (general conditions, line items, overhead, profit, insurance, contingency)

Value engineering (balancing cost vs. design changes)

Media/Content

Recorded lecture with annotated sample estimate

Interactive spreadsheet activity (adjusting for changes)

Assessments

Problem-based assignment: Review a sample estimate and propose cost savings

Short reflective journal: Tradeoffs between cost and design, where is the biggest bang for the buck?

Week 4 – Planning & Permitting

Topics

Construction plans & design workflow

Permitting processes and timelines

Role of inspections in moving the project forward

Media/Content

Demonstration video: From floor plan to permit (Bluebeam)

Reading: Sample permitting checklist

Simulation: Learners navigate a mock permitting process

Assessments

Quiz on permitting steps & required documentation

Forum: Share local permitting challenges learners have experienced or observed

Week 5 – Demolition & Site Preparation

Topics

Sample demolition plan

Working around existing mechanical systems

Preparing for construction

Media/Content
Photo gallery of demolition projects

Interactive drag-and-drop activity: Label demo plan elements

Guest speaker video: Demolition safety best practices

Assessments
Short essay: Risks & challenges in demolition phase

Knowledge check quiz

Week 6 – Construction & Inspections

Topics
Construction sequencing

Regular inspections and problem-solving onsite

Certificate of Occupancy / Temporary Certificates of Occupancy discussion

Media/Content
Timelapse video of construction stages

Reading: Sample inspection checklist

Case study: “Unexpected site issue and resolution”

Assessments
Scenario analysis: Learners identify inspection checkpoints on a sample timeline

Peer discussion: “How to handle the unexpected in construction projects”

Week 7 – Closeout & Documentation

Topics
Importance of final plans, finish schedules, equipment warranties

Managing closeout challenges

Professional integrity and communication during closeout

Media/Content
Checklist handout: Closeout essentials

Video tutorial: Compiling a closeout binder

Email writing exercise: Drafting professional closeout communication

Assessments
Practical assignment: Build a mock closeout checklist

Peer review of drafted closeout communications

Week 8 – Professional Growth & Final Assessment

Topics
Building a portfolio of construction projects

Networking and professional integrity

Course wrap-up & reflection

Media/Content
Portfolio showcase: FSU projects completed in 2024/2025 (virtual tour)

LinkedIn networking tips resource

Assessments
Flip the Script: Provide questions, interests, etc. for discussion in forum

Final quiz covering all modules

Reflection forum: “What I learned and how I’ll apply it”

Appendix B-Scope of Work (Videography)

Florida State University, Real Estate Center: Construction 101

POSITION	MEDIA COMPANY/VIDEOGRAPHER	
PERIOD OF PERFORMANCE (APPROX.)	Dec 31, 2025	March 2, 2026
MAXIMUM LEVEL OF EFFORT	30 hours	
BASE OF OPERATIONS	Tallahassee, FL	
POSITION REPORTS TO	Instructional Content Developer	

Background

This project will produce a course titled "Construction 101" for the FSU Real Estate Center introducing FSU students to construction sites, processes, and safety expectations. The goals of the project are to:

- Improve awareness of construction culture and etiquette.
- Emphasize the importance of safety when visiting or working near construction sites.
- Provide a foundational understanding of project estimates, permitting, construction processes, and inspections.
- Equip learners with practical knowledge of construction terminology, documents, and expectations.

Description of Services

Given the background, FSU requires an experienced media company or videographer to film construction sites and record interviews with experts in construction, safety, permitting, and inspections. These videos will be filmed and edited by the videographer into instructional content for the final project.

Tasks and Responsibilities

Activities to be carried out by the videographer include:

- Filming high-quality interviews with experts in the field
- Filming high-quality visits to construction sites on the FSU campus and/or in Tallahassee

- Filming or locating b-roll of construction site activities and processes
- Editing video, including bumpers, music, sound, and accurate captions in the finished videos

Activities and Deliverables

The contracted videographer will produce instructional videos of varying length between 5-15 minutes depending on requirements. Videographer will work with the Instructional Content Developer to provide critical feedback on storyboard ideas with best approaches to carry out video production. The videographer will meet with FSU staff and other stakeholders involved in the project.

Videos produced will comply with FSU marketing and branding, messaging, and style as identified in pre-production meetings with the Instructional Content Developer.

The videographer will deliver a final digital product optimized for web. All logos and credits will be provided, but videographer should suggest music or enhancements for the final version. FSU retains all ownership of raw and final footage.

The videographer will deliver copies of raw footage for each video and finished videos within 30 days of filming.

Level of Effort	**Activity**
Activity 1: Site visits	
2-3 days	Filming sites in Tallahassee
2-3 days	Filming sites at FSU
Activity 2: Expert interviews	
Film interviews with local construction site experts ~ 6 interviews	
Activity 3: Video editing	
Cut and edit video according to video storyboards and scripts, add lower thirds, logos and branding as appropriate	

Note: This scope of work is estimated based on site visits and profile interviews, editing and delivery. The timeline may be adjusted to reflect changes to site locations, interviewee availability, project timing, and project progress.

Reporting

The videographer and any staff they may employ reports to the project's Instructional Content Developer.

Qualifications

- Bachelor's degree in journalism or communication
- Experience producing instructional video, interviews, and on-site walkthroughs
- Experience on construction sites
- Strong storytelling and editing skills
- Ability to produce timely and high-quality video content

How to Apply

If interested please send the following to Project Manager, Construction 101, no later than December 2, 2025, to jgonzalez8@fsu.edu, with "**Construction 101/Videographer**" in the subject line:

- Resume with detailed professional experience
- Cover letter that explains your experience and why you are a good fit for the role
- Work samples or portfolio
- Three professional or academic references

Appendix C-Scope Change Request Form

Project Name: _____

Date of Request: _____

Requested By: _____

Description of Requested Change:

Justification / Reason for Change:

Impact on Scope: _____

Impact on Timeline: _____

Impact on Budget: _____

Impact on Quality or Deliverables: _____

Reviewed By (Project Manager): _____


Decision (Approve / Reject / Defer): _____

Sponsor Approval Signature: _____

Date of Decision: _____

Appendix D- Construction 101 Gantt Chart

October 23, 2025 | 19:14:12

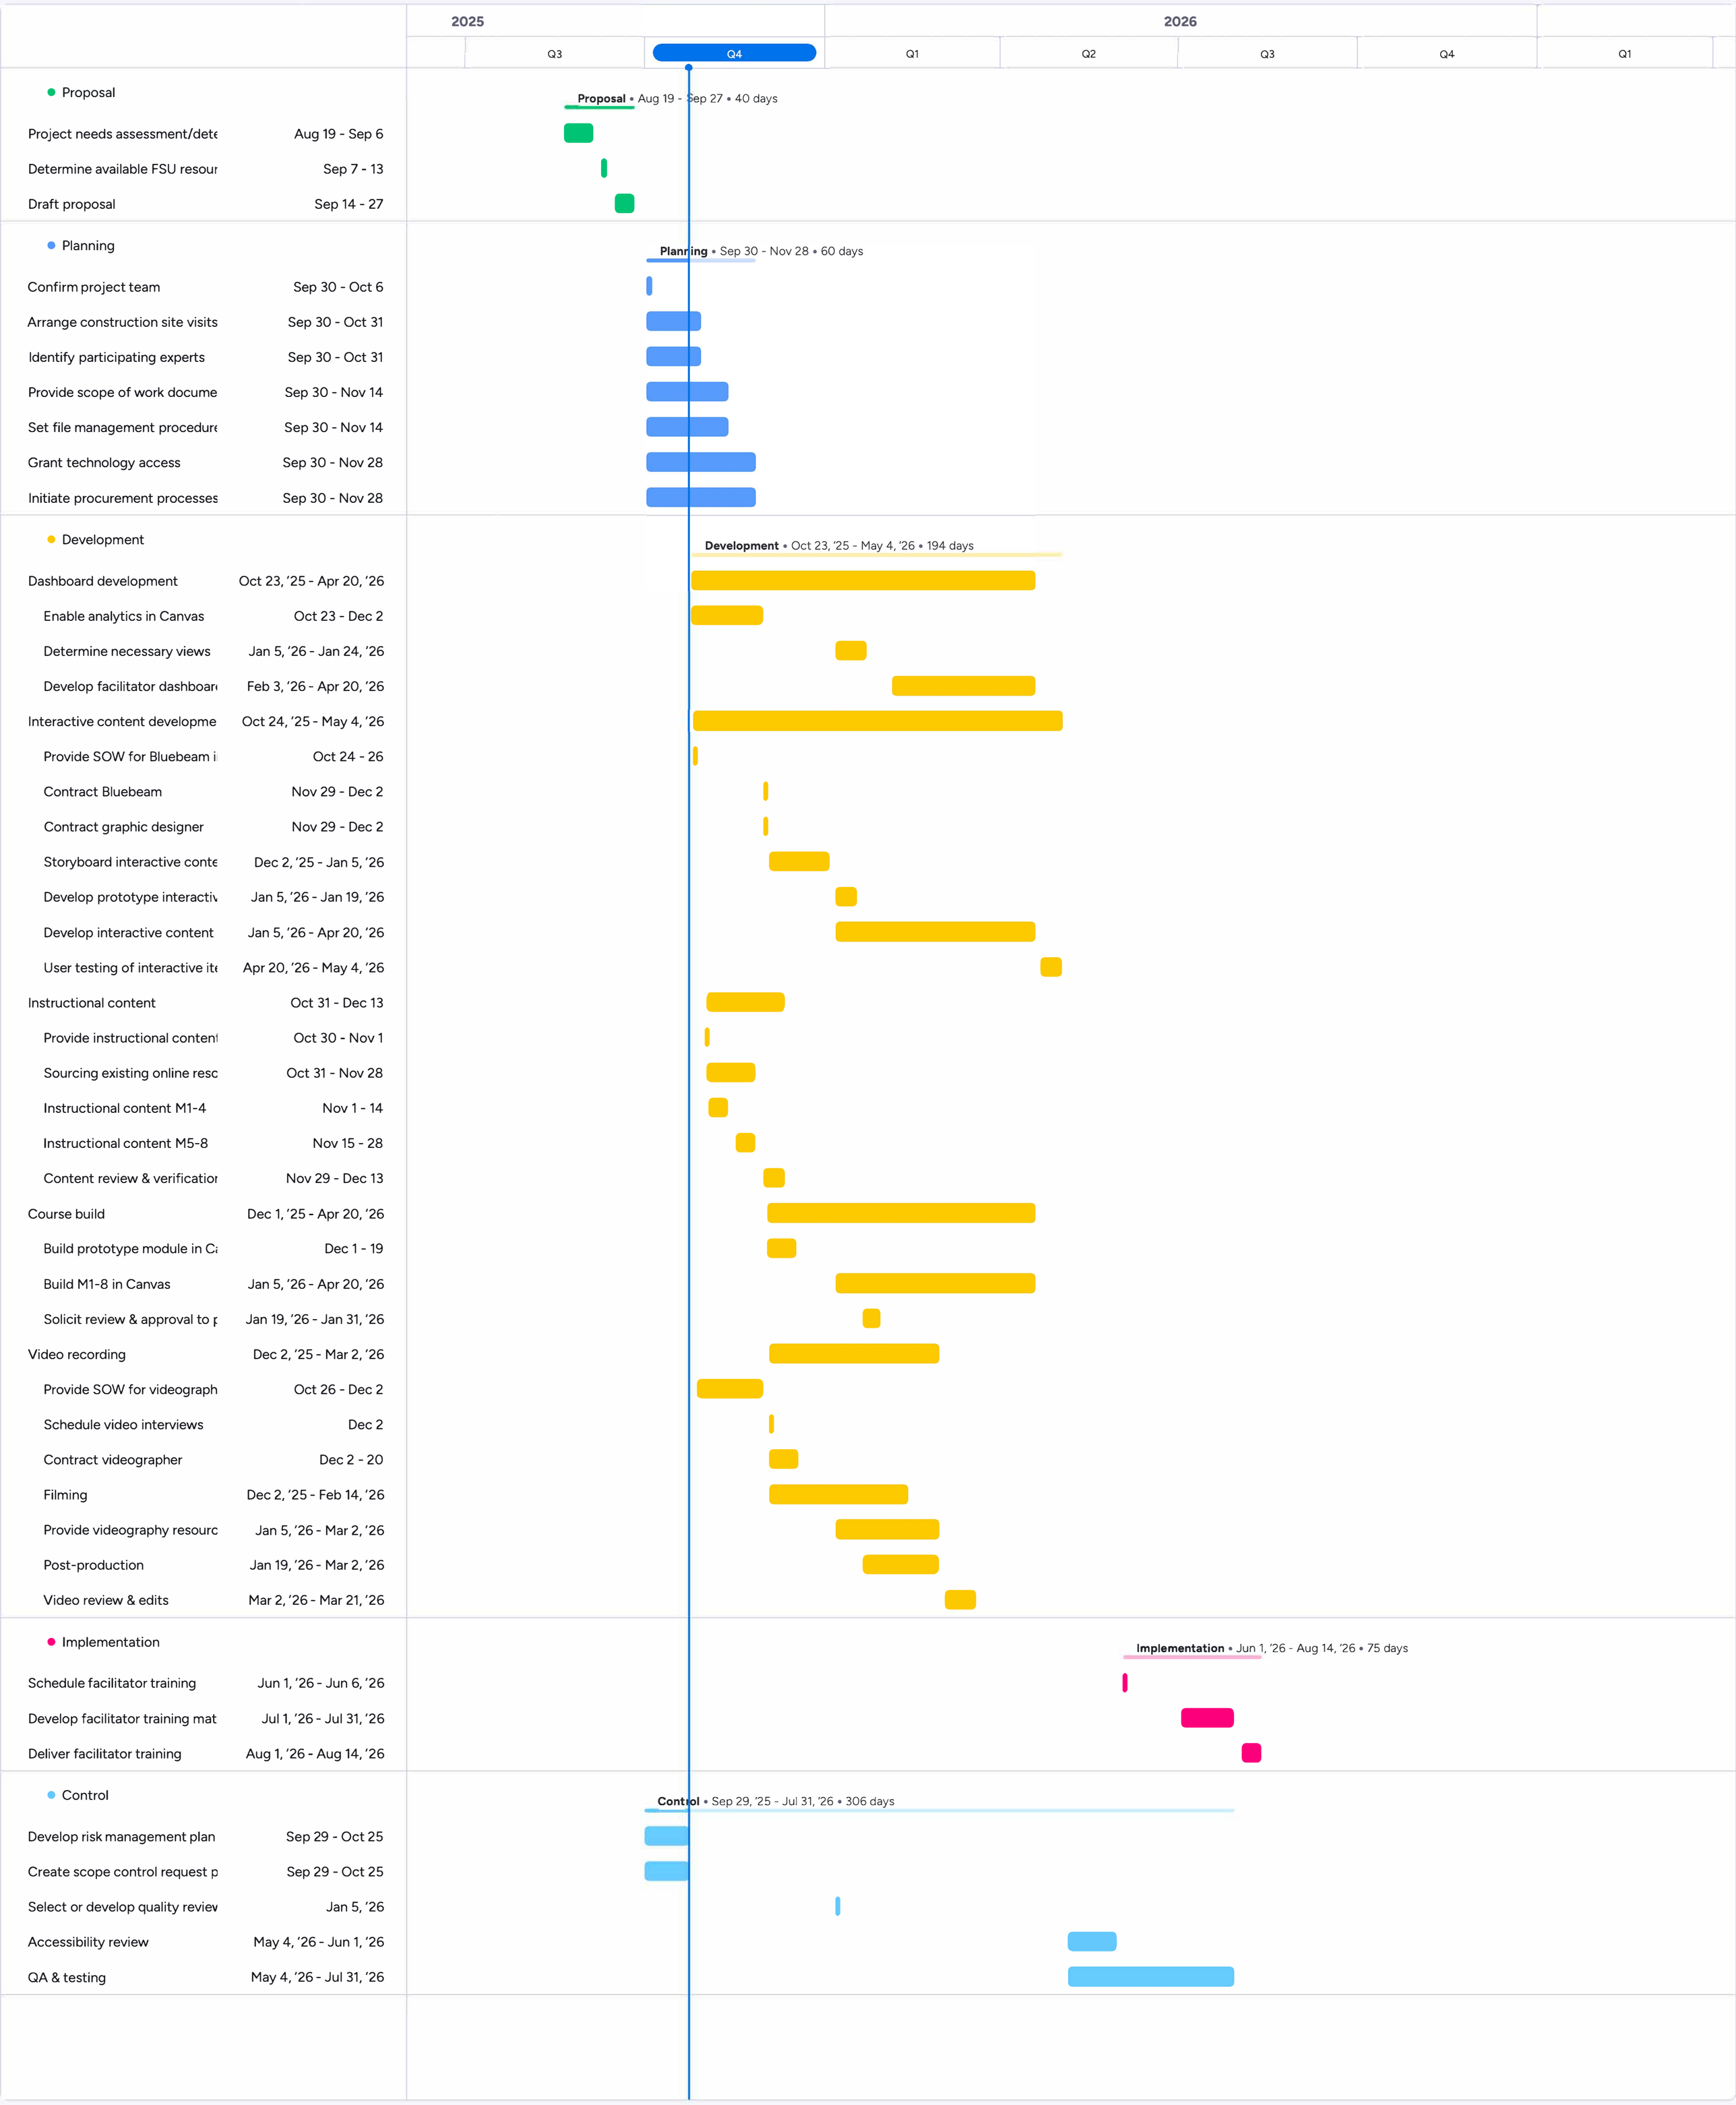

Appendix E- One-Page Project Manager (OPPM)

Project Manager: Jordan Gonzalez | **Project Name: Construction 101 Course** | Report Date: 24 Oct 2025

Project Objective: Creating and launching an online "Construction 101" course for FSU students.


Sub-Objectives				Major Tasks	❍ Work Planned in the Period / ● Planned Work Complete												Owners and Helpers			
❍			1	Determine student needs and FSU resources	●												A	B		
❍			2	Project planning & proposal	●													A	B	
❍			3	Confirm project team and set up shared file management site	●												A	B	C	
❍			4	Project kickoff & deliverable timeline	●												A	B	C	D
❍			5	Initiate contracted services	●	❍											A	B		
	❍		6	Arrange access to Canvas resources	❍	❍											A	C	B	
	❍		7	Arrange construction site visits	❍	❍	❍											A	C	B
❍			8	Instructional content modules 1-4 sourced and approved	❍	❍	❍	❍										A	C	B
❍			9	Instructional content modules 5-8 sourced and approved		❍	❍	❍	❍									A	C	B
	❍		10	Storyboard interactive content		❍	❍											B	A	C
	❍		11	Build prototype module			❍	❍	❍									B	A	C
	❍		12	Video content recording			❍	❍	❍								A	B	C	
	❍		13	Create interactive content					❍	❍	❍						C	B	A	
	❍		14	Build Canvas course site					❍	❍	❍						C	B	A	
	❍		15	Develop facilitator dashboard							❍	❍					C	B	A	
	❍		16	QA and testing									❍					C		B
		❍	17	Final client approval										❍			A	D	C	B
		❍	18	Close contracted services											❍		A	B		
		❍	19	Release course											❍		A			B
		❍	20	Course facilitation and dashboard analytics training											❍				A	B
		❍	21	Post-implementation feedback review												❍		A	C	B

				Risks Adequate / Worrisome / Dangerous	↑ Improving → Steady ↓ Worsening															
❍	❍		1	Timeline delays: Dependencies on video, SMEs, site scheduling	→													A		
❍	❍	❍	2	SME or stakeholder availability: scheduling conflicts	→														A	
❍	❍		3	Quality & accuracy: SME availability, construction complexity	→													A		
	❍		4	Budget overruns: Vendor hours or equipment needs	→												A			
❍	❍		5	Site & safety access: Campus access and weather conditions	→												A	A	A	
	❍	❍	6	Technology/LMS failure: Canvas or interactive tool limits	→															


Analysis & design of instructional content

Course development & implementation

Course deployed, facilitators trained

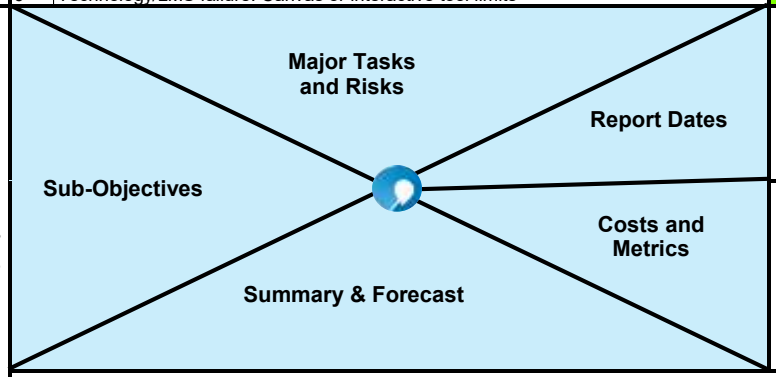

October	November	December	January	February	March	April	May	June	July	August	December	Jordan	Kim	Rebecca	Sadie/Dustin



Scope of work for videography, graphic design, and Bluebeam are being developed and contract deposits prepared.

Content development deadlines are upcoming.

Construction site selection and expert identification are underway.

Copyright OPPM International

Appendix F- Project Budget

Powered by monday.com

Manage any type of project.
Assign owners, set timelines

Planning

Name	Subitems	Owner	Status	Due date	Budget	Notes
Grant technology access			Working on it	2025-11-28	50	
					50	

Development

Name	Subitems	Owner	Status	Due date	Budget	Notes
Instructional content	Provide instructional content template,Instructional content M1-4,Instructional content M5-8,Sourcing existing online resources,Content review & verification		Not Started	2026-04-20	400	Bluebeam interactive graphics

Subitems	Name	Owner	Status	Date	Budget	Timeline - Start	Timeline - End	Notes
	Provide instructional content template			2025-10-31		2025-10-30	2025-11-01	Bluebeam interactive graphics
	Instructional content M1-4			2025-11-14		2025-11-01	2025-11-14	Content from SME
	Instructional content M5-8			2025-11-26		2025-11-15	2025-11-28	Content from SME
	Sourcing existing online resources			2025-11-26		2025-10-31	2025-11-28	In house labor
	Content review & verification			2025-12-13		2025-11-29	2025-12-13	In house labor

Interactive content development	uebeam interactives,Contract Bluebeam,Contract graphic designer,Storyboard interactive content for Storyline/Powerpoint,Develop prototype interactive content,Develop interactive content in Storyline/Powerpoint,User testing		Not Started	2026-05-04	750	Graphic designer		

Subitems	Name	Owner	Status	Date	Budget	Timeline - Start	Timeline - End	Notes
	Provide SOW for Bluebeam interactives			2025-10-26		2025-10-24	2025-10-26	
	Contract Bluebeam			2025-12-02	400	2025-11-29	2025-12-02	
	Contract graphic designer			2025-12-02	750	2025-11-29	2025-12-02	
	Storyboard interactive content for Storyline/Powerpoint			2026-01-05		2025-12-02	2026-01-05	
	Develop prototype interactive content			2026-01-19		2026-01-05	2026-01-19	
	Develop interactive content in Storyline/Powerpoint			2026-04-04		2026-01-05	2026-04-20	
	User testing of interactive items			2026-04-20		2026-04-20	2026-05-04	

Video recording and editing	Schedule video interviews,Provide SOW for videographer,Contract videographer,Provide videography resources (graphics, text for lower thirds, etc),Filming,Post-production,Video review & edits		Not Started	2026-02-28	1500	Videos at site visits, interviews		

Subitems	Name	Owner	Status	Date	Budget	Timeline - Start	Timeline - End	Notes
	Schedule video interviews				250	2025-12-02	2025-12-02	Order thank you food & beverage
	Provide SOW for videographer					2025-10-26	2025-12-02	
	Contract videographer				1500	2025-12-02	2025-12-20	Videographer contract costs
	Provide videography resources (graphics, text for lower thirds, etc)				450	2026-01-05	2026-03-02	Branded hard hats, materials
	Filming				100	2025-12-02	2026-02-14	Travel expenses for off-site
	Post-production					2026-01-19	2026-03-02	
	Video review & edits					2026-03-02	2026-03-21	

Course build	Build prototype module in Canvas,Solicit review & approval to proceed,Build M1-8 in Canvas		Not Started	2026-04-20	75	Software licensing		

Subitems	Name	Owner	Status	Date	Budget	Timeline - Start	Timeline - End	Notes
	Build prototype module in Canvas			2026-01-19		2025-12-01	2025-12-19	
	Solicit review & approval to proceed			2026-01-31		2026-01-19	2026-01-31	Utilize placeholder video & bluebeam
	Build M1-8 in Canvas			2026-04-20		2026-01-05	2026-04-20	
					6175			

Implementation

Name	Subitems	Owner	Status	Due date	Budget	Notes
Develop facilitator training materials		Kim Gabbard	Not Started	2026-07-31	250	Promotional materials
Schedule facilitator training		Kim Gabbard	Not Started	2026-06-05	100	Travel expense
Deliver facilitator training		Rebecca Yost	Not Started	2026-08-14	75	Misc office supplies for training
Obtain branded hard hats		Kim Gabbard	Not Started	2026-04-04	250	Order and ship
Obtain building sample materials, safety eq		Kim Gabbard	Not Started	2026-04-04	350	Order and label
Line up thank you food and beverage		Kim Gabbard	Not Started	2026-07-01	250	Get pricing, schedule
					1275	
